


Raspberry Falls & Selma Estates Water Treatment System Project



January 2018 Construction Schedule

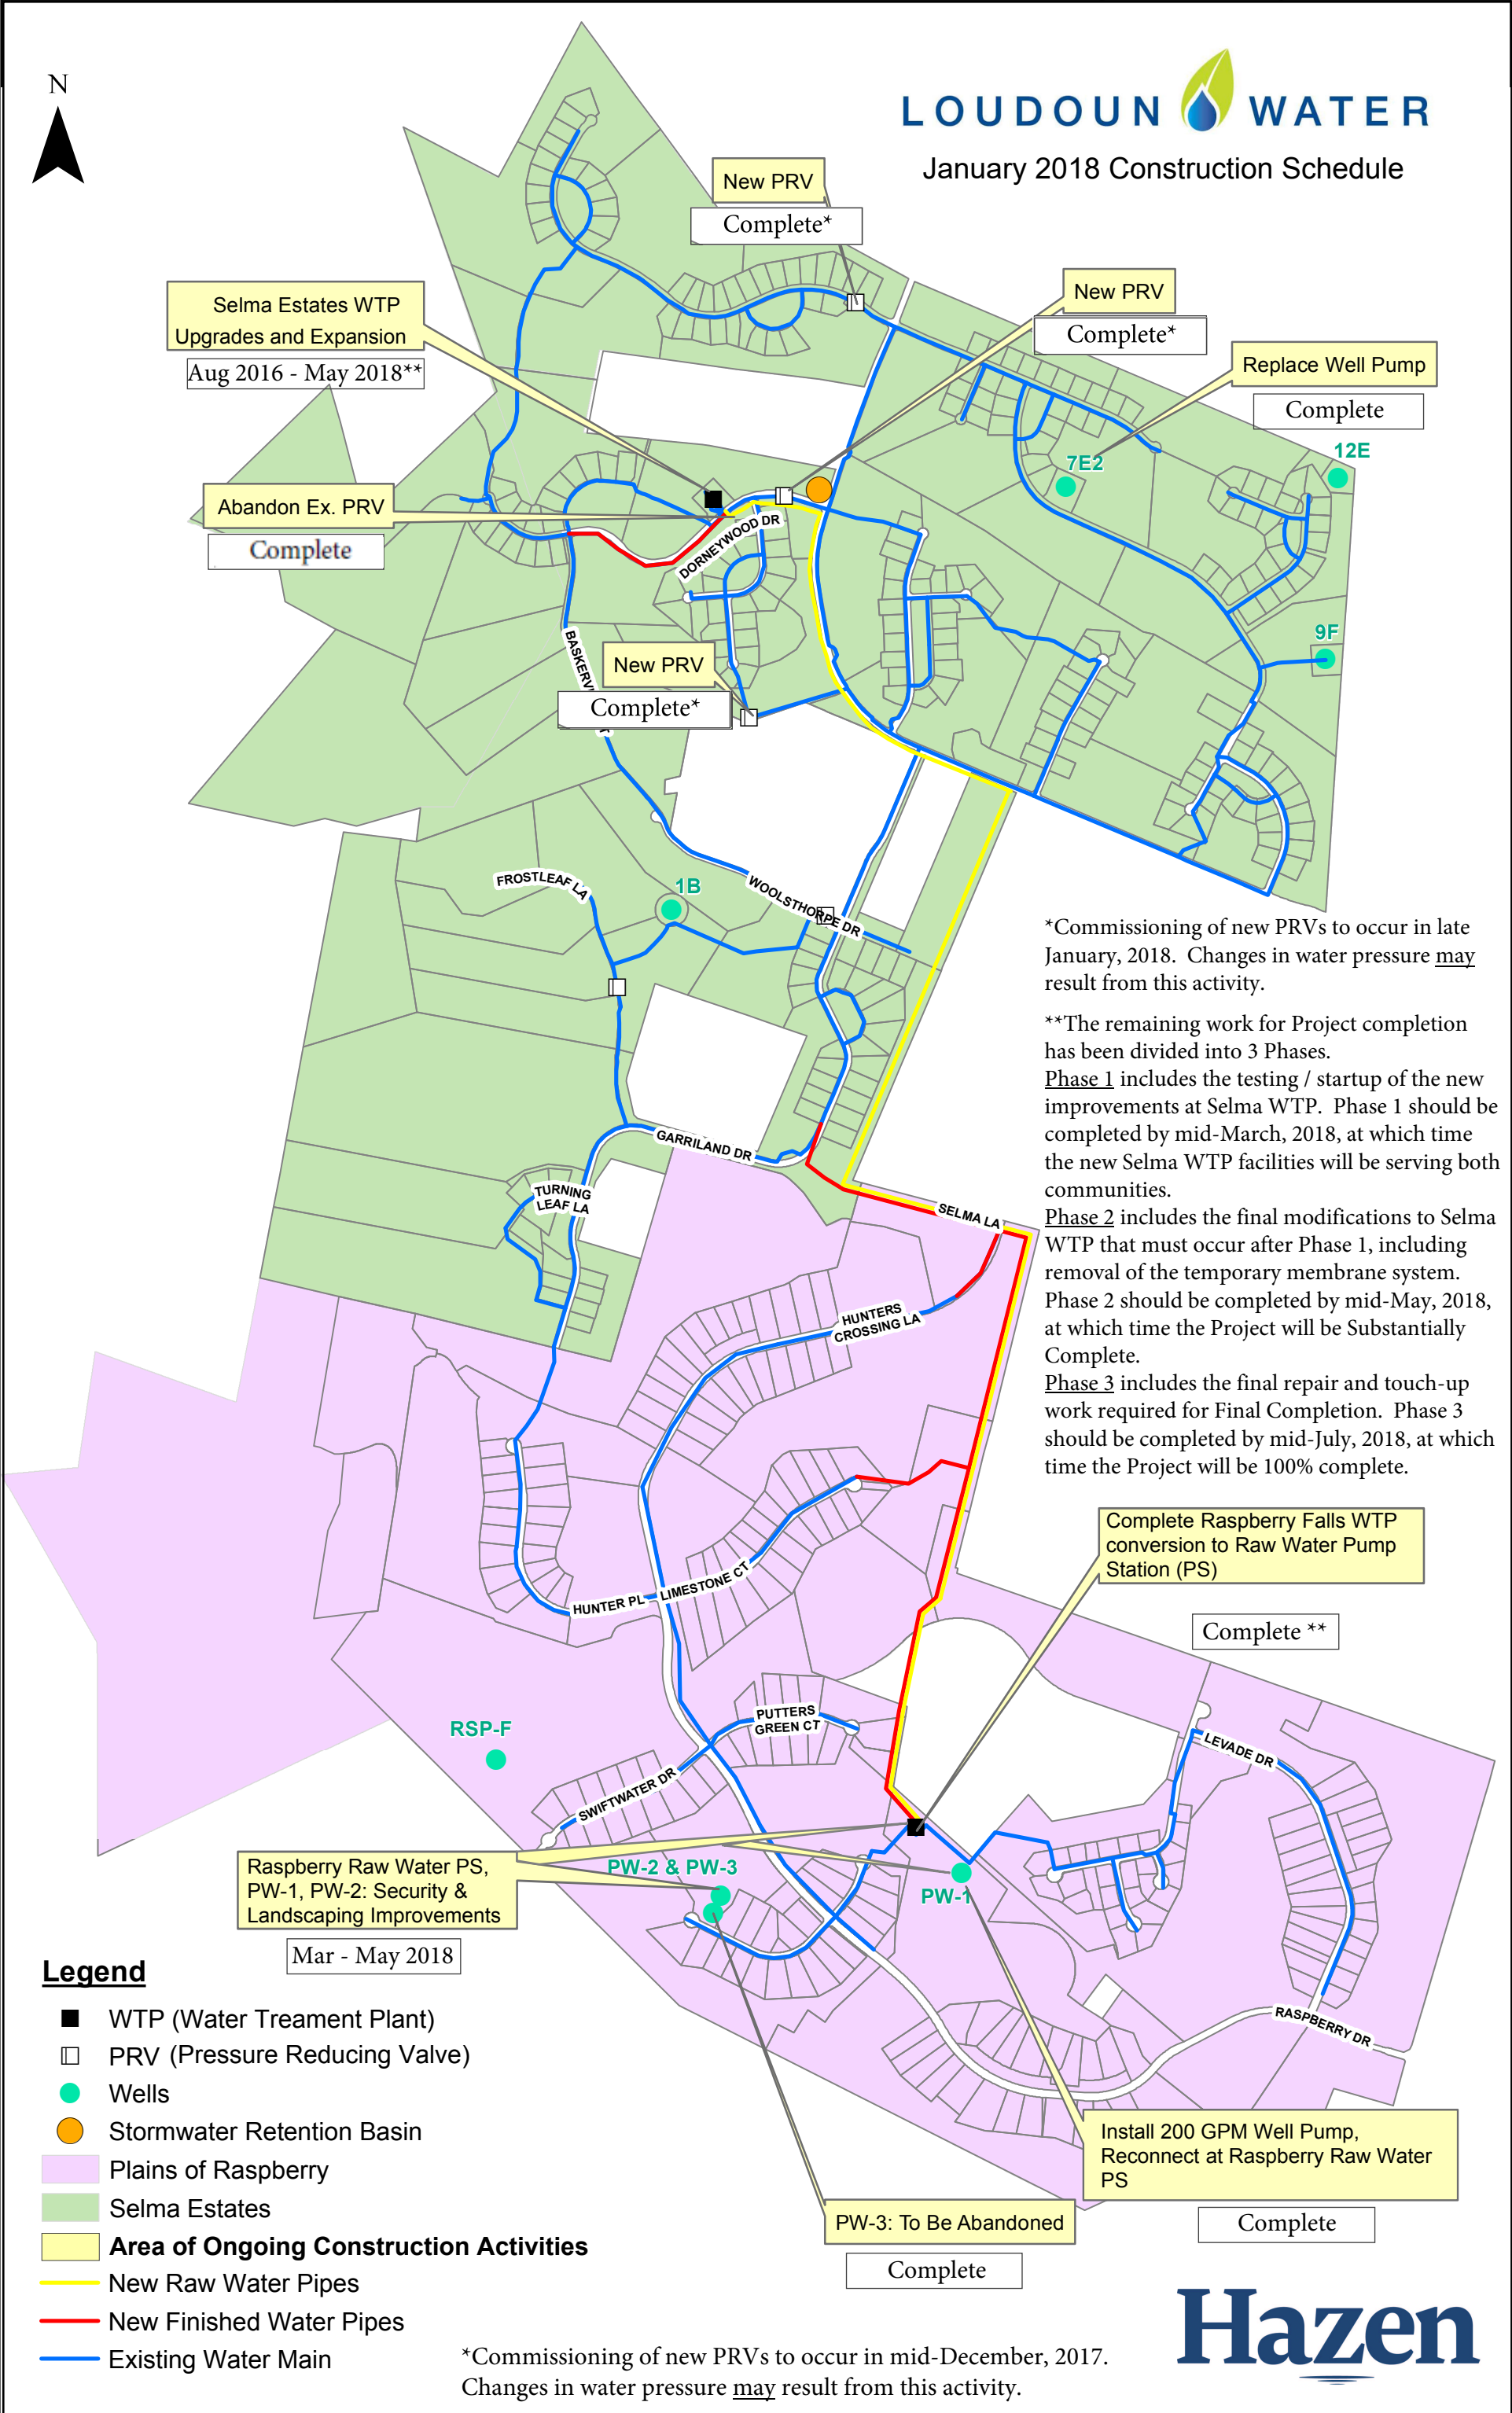

Selma Estates WTP Upgrades and Expansion
Aug 2016 - May 2018**

Abandon Ex. PRV
Complete

New PRV
Complete*

New PRV
Complete*

Replace Well Pump
Complete

New PRV
Complete*

*Commissioning of new PRVs to occur in late January, 2018. Changes in water pressure may result from this activity.

**The remaining work for Project completion has been divided into 3 Phases. Phase 1 includes the testing / startup of the new improvements at Selma WTP. Phase 1 should be completed by mid-March, 2018, at which time the new Selma WTP facilities will be serving both communities.

Phase 2 includes the final modifications to Selma WTP that must occur after Phase 1, including removal of the temporary membrane system. Phase 2 should be completed by mid-May, 2018, at which time the Project will be Substantially Complete.

Phase 3 includes the final repair and touch-up work required for Final Completion. Phase 3 should be completed by mid-July, 2018, at which time the Project will be 100% complete.

Complete Raspberry Falls WTP conversion to Raw Water Pump Station (PS)
Complete **

Raspberry Raw Water PS, PW-1, PW-2: Security & Landscaping Improvements
Mar - May 2018

Install 200 GPM Well Pump, Reconnect at Raspberry Raw Water PS
Complete

PW-3: To Be Abandoned
Complete

Legend

- WTP (Water Treatment Plant)
- PRV (Pressure Reducing Valve)
- Wells
- Stormwater Retention Basin
- Plains of Raspberry
- Selma Estates
- Area of Ongoing Construction Activities
- New Raw Water Pipes
- New Finished Water Pipes
- Existing Water Main

*Commissioning of new PRVs to occur in mid-December, 2017. Changes in water pressure may result from this activity.

